Report to Hon. Thomas P. Olivieri

Partial Consent Judgment Concerning PPG Sites

Site Administrator W. Michael McCabe

March 9, 2010



N.J. DEPARTMENT OF ENVIRONMENTAL PROTECTION CITY OF JERSEY CITY PPG INDUSTRIES COURT-APPOINTED SITE ADMINISTRATOR

Settlement Compliance - First Steps

Settlement Entered - 6/26/09

Site Administrator - Appointed: 7/6/09

- n Planning/Organization Starts
- n Site Administrator Program Manager hired
- n Site Administrator legal representation hired

Organizational Meeting – Held: 8/3/09

- n Tasks/goals required by settlement identified
- n Task work groups established
- n Criteria for Technical Consultant developed

Technical Consultant Search/Selection - On board: 10/26/09

- n Search based on qualifications criteria
- n RFQ sent to 30+ firms

Settlement Requirements - Compliance Actions

Master Schedule Development – Public Draft: 11/19/09

- n Work group collaboration
- n Reviewed prior assumptions, investigation and planning
- n Prioritized and staged all 20 PPG sites
- n Compressed 10-year plan into 5
- n More than 1200 tasks for Garfield Ave. site
- n Technical Consultant review
- n Community public meeting 11/23/09

Master Schedule Official Start Date – 12/01/09

- n Superior Court notification: 12/01/09
- n Master Schedule tracking commences

Master Schedule for PPG Chromium Sites 2010 2011 2012 2013 2014 SITE Garfield Avenue Group Alternative 1: Full Excavation (Sites 114, 132, 133, 135, OR 137, 143 and 186) Slab Demolition Targeted Excavation Alternative 2: Targeted Excavation & Treatment Treatment Testing **Berry Lane Group** (Sites 121 and 207) Sampling Work Plans **Metropolis Towers** (Sites 156) Remediation Work Plans Dennis Collins Park DEP Alternative Evaluation (Sites 174) **Claremont Associates** Delineation (Sites 203) Initial Remediation Program **Conrail Edgewater** Data Analysis & Assessment (Sites 204) Fashionland/Albanil (Sites 107/108) Completion Linden Avenue East (Sites 16) Baldwin/Burma (Sites 63/65) **Commerce Street** (Sites 146) **Caven Point Realty** (Sites 202)




Settlement Requirements

- Compliance Actions, continued

Residential Inspection/Cleanup Program – Launch: 1/21/10

- n Established "hotline" call-in number
- n Developed three-stage process for responding to residents' calls
- n Assembled experts to inspect, sample and remediate
- n Community workshop 1/21/10
- n 20 requests to date

Residential Inspection Program Process

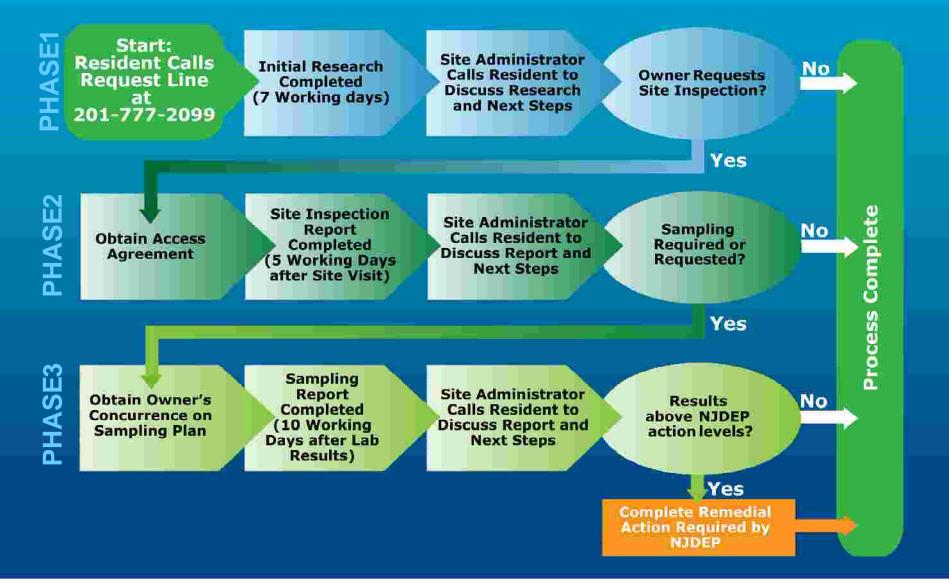

Settlement Requirements - Compliance Actions, continued

Health Study – Preliminary Recommendation: 2/8/10

- n December deadline extended awaiting Jersey City-based ATSDR cancer study
- n Determined need and value to residents
- n Focused on community concerns related to remediation activity and exposure potential
- n Reviewed 50+ health studies
- n Consulted 20 experts
- n Community Review TBA

Settlement Requirements

- Compliance Actions, continued

20% Jersey City Hiring Goal


- n Reached agreement with Jersey City on the scope of the program. Most employment opportunities expected to be on-site union labor positions required for remediation activities.
- n Initial Community review 11/23/09.
- n Met with Operating Engineers Union on 12/9/09.
- n Scheduled to meet with Laborers Union on 2/10/10.
- n Local hiring requirements to be incorporated in bid documents.
- n Major field activity scheduled to begin in June 2010.

Settlement Requirements - Compliance Actions, continued

Community Outreach - Ongoing

- n Established local phone number
- n Launched Web site www.chromecleanup.com
- n Developed unifying graphics/logo to identify work products/informational material
- n Maintained PPG storefront and activities
- n Mayor established Citizen Advisory Board
- n Mailed newsletter report to 4,500 residents
- n Distributed/mailed fliers announcing meetings/contact info
- n Conducted small group outreach
- n Held public meetings in November, December, January

Newsletter



www.chromachanug.com.

Quay for inspection

the Chronouni Cognico Decisionahia tale Sent special description of held produces one

Phone: 20) 777-7099 | Http://www.chrumecleanup.com. | < 2000 Civismuir Cleanup Derriembre

Welcows from Airba

Was Administrator MinoriseCube Numbers hear

Chromium Cleanup Partnership

Fliers to Residents

Chromium Cleanup

Partnership

Partnership

Tell Us What You Think Chrome and Your Health

The Chromium Cleanup Partnership is conducting public meetings in conjunction with cleanups PPG Industries will perform in Jersey City and Bayonne. All residents and interested parties are welcome to attend and share their thoughts. No preregistration is required.



Thursday, December 17 (New location, Previously scheduled for Dec.14) Topic:

Determine need for future community health studies Location: Gothic Lounge (Room 202)


Hepburn Hall

New Jersey City University 2039 Kennedy Blvd.

Jersey City

Time: 6:30 p.m.

New Jersey City University is eccessible by NJ Transk bus rouses 10 and 80, and the Hudson-Bargen Light Pail (West Side Avenue) Parking will be validated.



January 21 Tapic:

Workshop on residential chrome sempling and clearup program Location:

140 Martin Lusher King Driva dersey City

Time; 6:30 p.m.

For more information:

Phone: 201777/2095

Wab site, http://www.chromaclearup.com

PPG roffice PPG s Garfield Avenue Retrewal Company 334 Martin Luthen King Drive, Jersey City Toesdays and Thursdays, to a.m., to 2 p.m., and by appointment



